




CERTIFIED LEAKAGE REPORT


Duct sealing performed for:



Phone: [Redacted]
Square Footage: 2270

Technician Name: 7522
Date: 11/15/2024

Leakage (CFM₂₅)

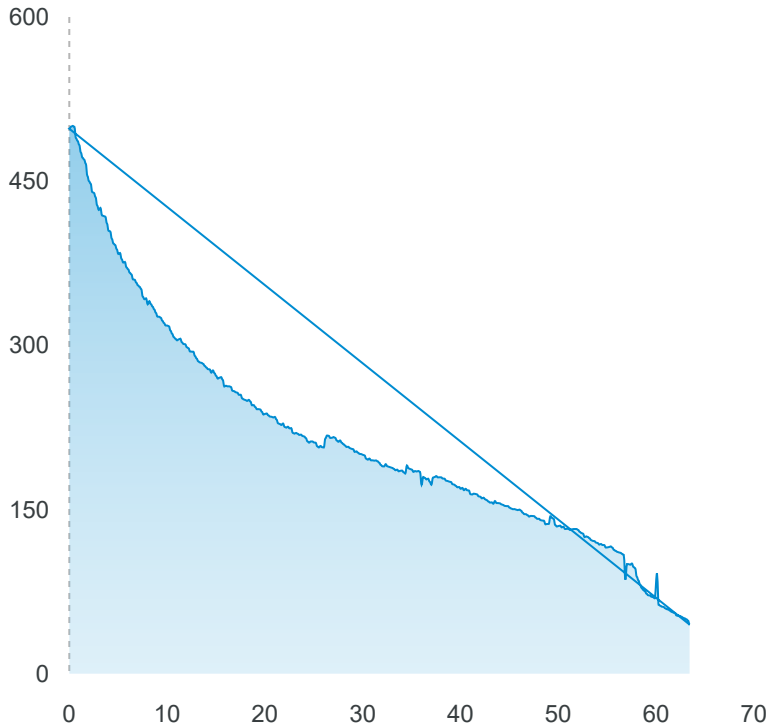

Duct leakage results are calculated in Cubic Feet per Minute (CFM) calculated at a STANDARD OPERATING PRESSURE of 25 Pa.

Going Beyond Any Other Energy Reduction Service



Improved Indoor Air Quality



Improved Efficiency



Increased Home Comfort

Scan for more details



Aeroseal
aeroseal.com
877-FIX-DUCT
info@aeroseal.com

Aeroseal Case ID: 7522

System Description: Heating System

Seal Whole Home Forced Hot Air

Description: Furnace

Hardware: HomeSeal Advance

	Initial	Final
CFM ₂₅	498	45
CFM ₂₅ /100 ft ²	21.9	2.0
Equivalent Hole Size	94.1 in ²	8.5 in ²
% System Capacity	17.8%	1.6%



Duct sealing performed by:

Lord Building Solutions
60 Browns Way
North Yarmouth, ME 04097
Phone: (207) 870 7391



**LORD
BUILDING
SOLUTIONS**
