



CERTIFIED LEAKAGE REPORT

Duct sealing performed for:

Avesta Housing - Meadowview II
16 Hancock St
04039, ME 04039
Phone:
Square Footage: 9765

Technician Name:7522
Date:11/21/2024


Aeroseal Case ID:7522

System Description:Ventilation System - ERV

Seal Description:First Floor

Hardware:HomeSeal Advance

Leakage (CFM₂₅)

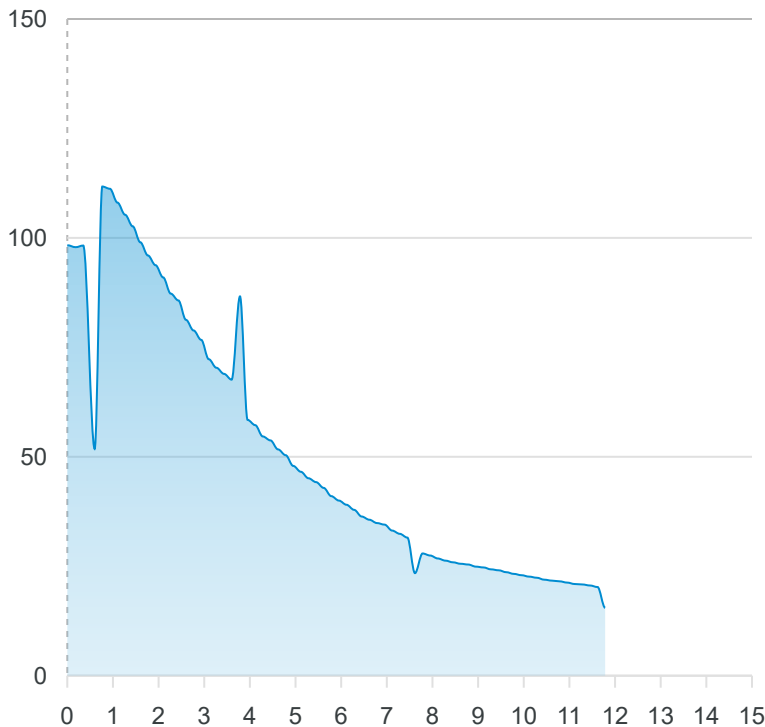

Duct leakage results are calculated in Cubic Feet per Minute (CFM) calculated at a STANDARD OPERATING PRESSURE of 25 Pa.

Going Beyond Any Other Energy Reduction Service



Improved Indoor Air Quality



Improved Efficiency



Increased Home Comfort

	Initial	Final
CFM ₂₅	98	16
CFM ₂₅ /100 ft ²	1.0	.2
Equivalent Hole Size	18.6 in ²	2.9 in ²
% System Capacity	7.0%	1.1%



Scan for more details



Aeroseal
aeroseal.com
877-FIX-DUCT
info@aeroseal.com

Duct sealing performed by:

Lord Building Solutions
60 Browns Way
North Yarmouth, ME 04097
Phone: (207) 870 7391



**LORD
BUILDING
SOLUTIONS**
